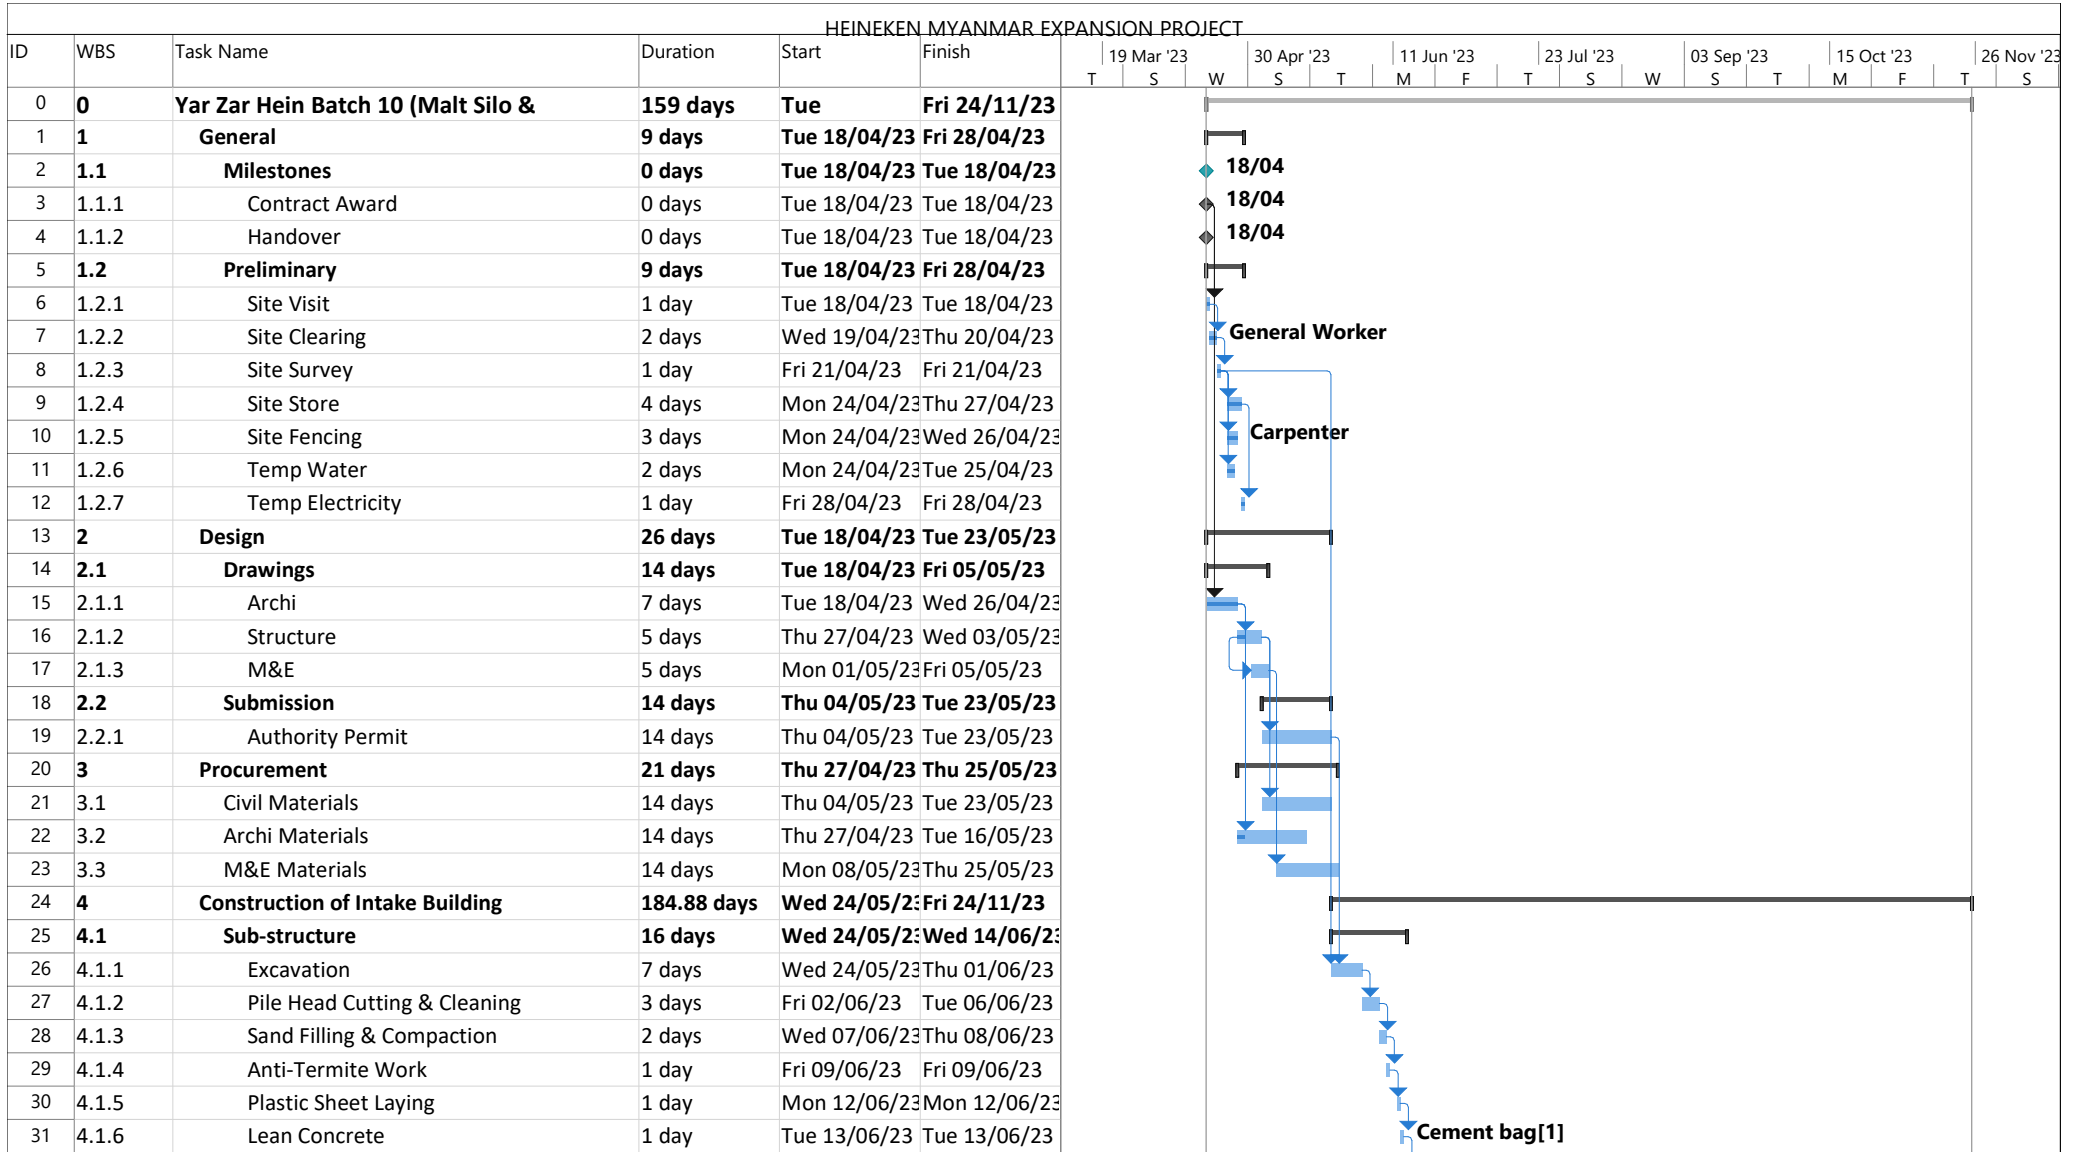




Project: Yar Zar Hein Batch 10 (

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone



Deadline

Progress

Manual Progress

Page 1

HEINEKEN MYANMAR EXPANSION PROJECT																									
ID	WBS	Task Name	Duration	Start	Finish	19 Mar '23			30 Apr '23			11 Jun '23			23 Jul '23			03 Sep '23			15 Oct '23			26 Nov '23	
						T	S	W	S	T		M	F	T	S	W	S	T		M	F	T	S		
32	4.1.7	Waterproof Membrane Sheet	1 day	Wed 14/06/23	Wed 14/06/23																				
33	4.2	Base Slab Footng	54 days	Thu 15/06/23	Tue 29/08/23																				
34	4.2.1	Footng Rebars	5 days	Thu 15/06/23	Wed 21/06/23																				
35	4.2.2	Column Rebars	1 day	Thu 22/06/23	Thu 22/06/23																				
36	4.2.3	Footng Formworks	2 days	Fri 23/06/23	Mon 26/06/23																				
37	4.2.4	Water Stopper Installation	1 day	Tue 27/06/23	Tue 27/06/23																				
38	4.2.5	Footng Casting	1 day	Wed 28/06/23	Wed 28/06/23																				
39	4.2.6	Base Slab Polishing	1 day	Thu 29/06/23	Thu 29/06/23																				
40	4.2.7	Basement Wall	20 days	Fri 30/06/23	Thu 27/07/23																				
41	4.2.7.1	Wall Rebars	4 days	Fri 30/06/23	Wed 05/07/23																				
42	4.2.7.2	Wall Formworks	14 days	Thu 06/07/23	Tue 25/07/23																				
43	4.2.7.3	Stainless Steel Ladder	1 day	Wed 26/07/23	Wed 26/07/23																				
44	4.2.7.4	Wall Concreting Work	1 day	Thu 27/07/23	Thu 27/07/23																				
45	4.2.8	Intake Pit Top Slab	23 days	Fri 28/07/23	Tue 29/08/23																				
46	4.2.8.1	Scaffolding Work	7 days	Fri 28/07/23	Mon 07/08/23																				
47	4.2.8.2	Slab Beam FormWork	7 days	Tue 08/08/23	Wed 16/08/23																				
48	4.2.8.3	Slab Rebars Work	5 days	Thu 17/08/23	Wed 23/08/23																				
49	4.2.8.4	Anchor Bolt Installation	2 days	Thu 24/08/23	Fri 25/08/23																				
50	4.2.8.5	Top Slab Concreting	1 day	Mon 28/08/23	Mon 28/08/23																				
51	4.2.8.6	Top Slab Polishing	1 day	Tue 29/08/23	Tue 29/08/23																				
52	4.3	Construction of Treatment Building	86 days	Fri 28/07/23	Fri 24/11/23																				
53	4.3.1	Sub-Structure	18 days	Fri 28/07/23	Tue 22/08/23																				
54	4.3.1.1	Excavation	7 days	Fri 28/07/23	Mon 07/08/23																				
55	4.3.1.2	Pile Head Cutting & Cleaning	5 days	Tue 08/08/23	Mon 14/08/23																				
56	4.3.1.3	Sand Filling & Compaction	3 days	Tue 15/08/23	Thu 17/08/23																				
57	4.3.1.4	Plastic Sheet Laying	1 day	Fri 18/08/23	Fri 18/08/23																				
58	4.3.1.5	Anti-Termite Work	1 day	Mon 21/08/23	Mon 21/08/23																				
59	4.3.1.6	Lean concrete	1 day	Tue 22/08/23	Tue 22/08/23																				
60	4.3.2	F1 Pile Cap Footing	9 days	Wed 23/08/23	Mon 04/09/23																				
61	4.3.2.1	Footng Rebars	7 days	Wed 23/08/23	Thu 31/08/23																				
62	4.3.2.2	Footng Casting	2 days	Fri 01/09/23	Mon 04/09/23																				
63	4.3.3	Short Column for F1 Pile Cap (16 Nos)	5 days	Tue 05/09/23	Mon 11/09/23																				

Project: Yar Zar Hein Batch 10 (	Task		Inactive Task		Manual Summary Rollup		External Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline	
	Milestone		Inactive Summary		Start-only		Progress	
	Summary		Manual Task		Finish-only		Manual Progress	
	Project Summary		Duration-only		External Tasks			

HEINEKEN MYANMAR EXPANSION PROJECT																							
ID	WBS	Task Name	Duration	Start	Finish	19 Mar '23			30 Apr '23		11 Jun '23		23 Jul '23		03 Sep '23			15 Oct '23		26 Nov '23			
						T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S		
64	4.3.3.1	Column Rebars	2 days	Tue 05/09/23	Wed 06/09/23																		
65	4.3.3.2	Column Formworks	2 days	Thu 07/09/23	Fri 08/09/23																		
66	4.3.3.3	Column Concreting	1 day	Mon 11/09/23	Mon 11/09/23																		
67	4.3.4	F0 Drop Cap Footing (20 Nos)	19 days	Tue 12/09/23	Fri 06/10/23																		
68	4.3.4.1	Pile Head Cutting & Cleaning	4 days	Tue 12/09/23	Fri 15/09/23																		
69	4.3.4.2	Sand Filling & Compaction	2 days	Mon 18/09/23	Tue 19/09/23																		
70	4.3.4.3	Anti-Termite Work	1 day	Wed 20/09/23	Wed 20/09/23																		
71	4.3.4.4	Plastic Sheet Laying	1 day	Thu 21/09/23	Thu 21/09/23																		
72	4.3.4.5	Lean Concrete	1 day	Fri 22/09/23	Fri 22/09/23																		
73	4.3.4.6	9" thk Brick Work	4 days	Mon 25/09/23	Thu 28/09/23																		
74	4.3.4.7	Dro Cap Rebars Work	4 days	Fri 29/09/23	Wed 04/10/23																		
75	4.3.4.8	Drop Cap Concreting	2 days	Thu 05/10/23	Fri 06/10/23																		
76	4.3.5	Ground Beam	14 days	Mon 09/10/23	Thu 26/10/23																		
77	4.3.5.1	Sand Filling & Compaction	2 days	Mon 09/10/23	Tue 10/10/23																		
78	4.3.5.2	Anti-Termite Work	1 day	Wed 11/10/23	Wed 11/10/23																		
79	4.3.5.3	Plastic Sheet Laying	1 day	Thu 12/10/23	Thu 12/10/23																		
80	4.3.5.4	Lean Concrete	2 days	Fri 13/10/23	Mon 16/10/23																		
81	4.3.5.5	Ground Floor Brick Work	4 days	Tue 17/10/23	Fri 20/10/23																		
82	4.3.5.6	Ground Beam Rebars	4 days	Tue 17/10/23	Fri 20/10/23																		
83	4.3.5.7	Ground Formworks	4 days	Mon 23/10/23	Thu 26/10/23																		
84	4.3.6	Treatment Building Floor Slab	21 days	Fri 27/10/23	Fri 24/11/23																		
85	4.3.6.1	Sand Filling & Compaction	5 days	Fri 27/10/23	Thu 02/11/23																		
86	4.3.6.2	Anti-Termite Work	1 day	Fri 03/11/23	Fri 03/11/23																		
87	4.3.6.3	Plastic Sheet Laying	1 day	Mon 06/11/23	Mon 06/11/23																		
88	4.3.6.4	Lean Concrete	1 day	Tue 07/11/23	Tue 07/11/23																		
89	4.3.6.5	Stainless Steel Gutter Installation	3 days	Wed	Fri 10/11/23																		
90	4.3.6.6	Floor Slab Rebars Work	4 days	Mon 13/11/23	Thu 16/11/23																		
91	4.3.6.7	Floor Slab Formworks	4 days	Fri 17/11/23	Wed 22/11/23																		
92	4.3.6.8	Floor Slab Concreting	1 day	Thu 23/11/23	Thu 23/11/23																		
93	4.3.6.9	Floor Hardner Polishing	1 day	Fri 24/11/23	Fri 24/11/23																		

Project: Yar Zar Hein Batch 10 (	Task		Inactive Task		Manual Summary Rollup		External Milestone		
	Split		Inactive Milestone		Manual Summary		Deadline		
	Milestone		Inactive Summary		Start-only		Progress		
	Summary		Manual Task		Finish-only		Manual Progress		
	Project Summary		Duration-only		External Tasks				
Page 3									
